
Hassocks


Hope & Clay (Construction) Ltd

A


					Ju				Aug					Se			1		Oct				Nov	
ID	Name	Start	Finish	Duration				5	12	19	26	2		9	16	23	30	7	14	<mark> 21</mark>	28			
					1	2		3	4	5	6	7		8	9	10	11	12	13	14	15	16	6 17	<u>18</u>
1	Crossroads						. 0		//				- 🖉 -	_								<u>_</u>		
2									//				- 🖉 –	_								🏽		
3	Close Road	24/07/19	02/09/19	29d							·	R –		_								/ ·		
4	4 Way Temporary Traffic Lights	03/09/19	08/11/19	49d										_								/ ·		
5	TM to be removed for London to Brighton Car Ru	01/11/19	01/11/19	0d					//		[<u> </u>		_		TT	m Off	Road f	for Wee	kend O	nly 🔶	<u>_</u>		
6											[<u> </u>										Ø		
7	Construct Retaining Walls & Steps	24/07/19	13/08/19	15d					<u> </u>		[_								Ø		
8	Remove Existing Signals	24/07/19	26/07/19	3d					//		[<u> </u>	_								<u>_</u> .		
9	Excavate Southern Widening	29/07/19	30/07/19	2d		_			//				<u> </u>	_								<u>_</u> .		
10	Stone Up	31/07/19	01/08/19	2d		0			//					_				1[<u>_</u> .		
11	Gullies	02/08/19	02/08/19	1d					🛛		[<u> </u>	<u> </u>	_ 0				1[<u>_</u> .		
12	Kerbing	05/08/19	06/08/19	2d							[<u> </u>	<u> </u>	_0								<u>_</u> .		
13	Overrun Strip	07/08/19	12/08/19	4d					/			<u> </u>	8_	_	//							ĺ.		
14	Breakup Existing Islands	13/08/19	15/08/19	3d									8_									<u>_</u> .		
15	Signal Ducting	11/09/19	26/09/19	12d								<u></u>										Ø		
16	Construct Islands	16/08/19	20/08/19	3d																		//		
17	Nal Sockets	21/08/19	23/08/19	3d	T																	//		
18	Tactiles	26/08/19	27/08/19	2d																		//		
19	Reconstruct London Road Island	28/08/19	30/08/19	3d																		//		
20	Signals Ducting Across London Road	28/08/19	30/08/19	3d														[[//		
21	Signals Ducting Keymar Road	02/09/19	10/09/19	7d																		//		
22	Tactiles										. – –			_					[/		
23	Signals Ducting London Road South Bound	11/09/19	27/09/19	13d							. – –											//		
24	Signals Ducting London Road North Bound	30/09/19	16/10/19	13d									10-	- 0								/		
25	Street Lighting	17/10/19	23/10/19	5d							. – –		-	-					- 1-			//		
26													10 -	-0				[7-		/ /		
27	Signals Installation	21/10/19	08/11/19	15d									10 -	-0										
28	Signage	22/10/19	23/10/19	2d									10 -	- 0		[[[·/		
29	Surfacing	24/10/19	25/10/19	2d									10 -	- 0						I -				
30	Road Markings	08/11/19	08/11/19	1d									1	-									· · · ·	
	4 Way Temp Lights Veteran Car Run TM Road Closure																							

Rev B

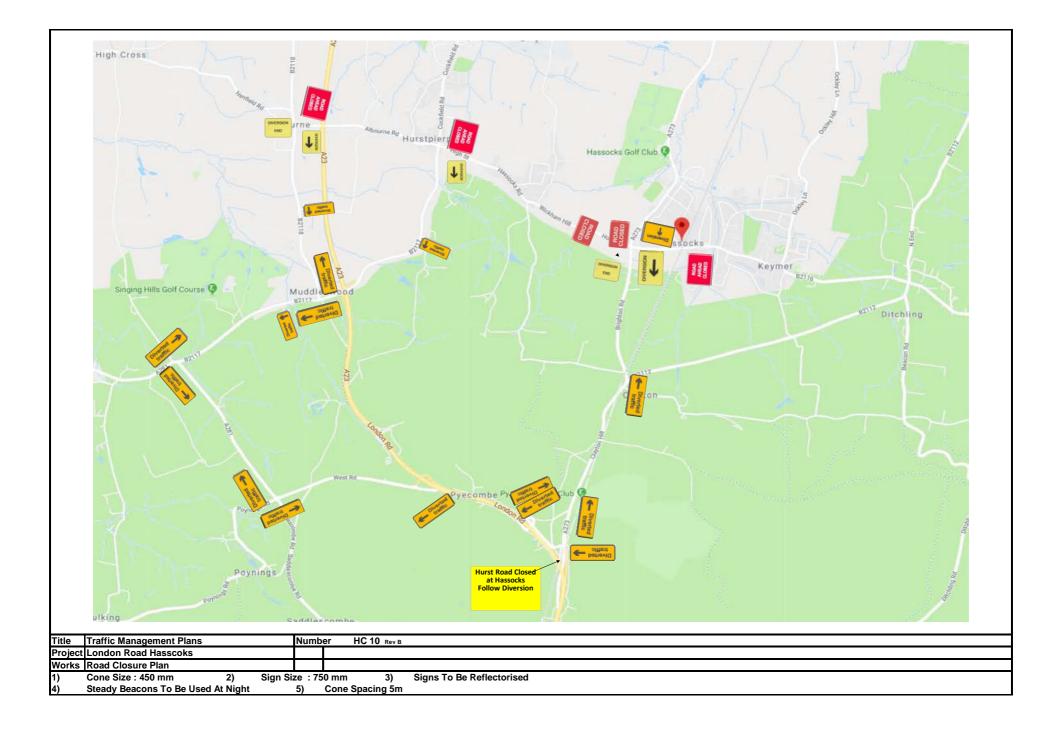


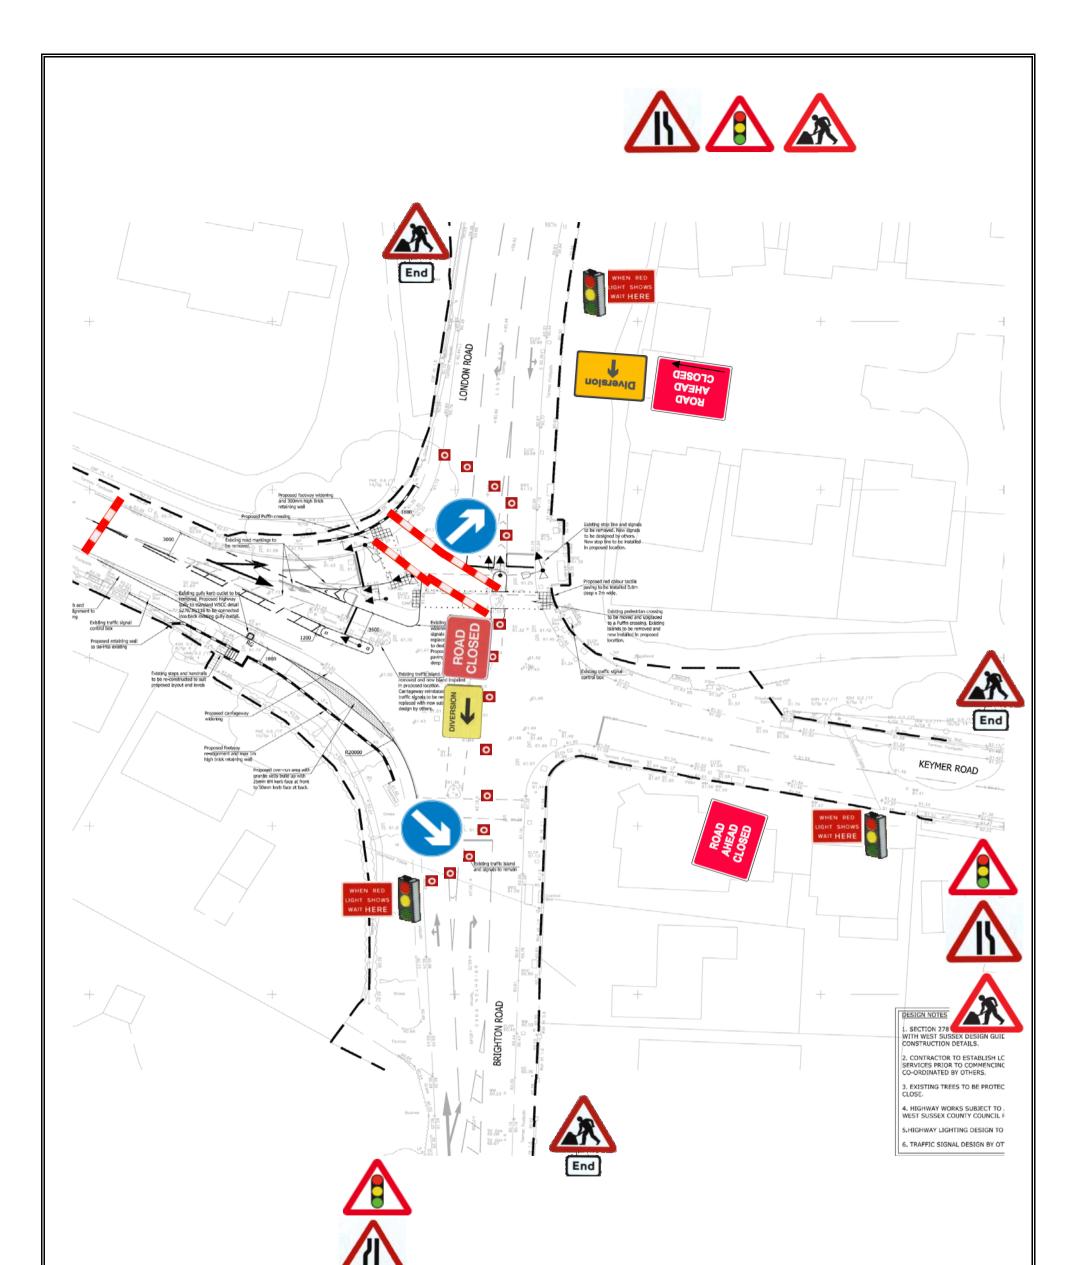

Title	Traffic Management Plans	Number	HC 15	
Project	London Road, Hassocks, New Site Entrance			
Works	S278			
1)	Cone Size : 750 mm	6)	24 Hour Traffic Lights	
2)	Sign Size :750 mm			
3)	Signs To Be Reflectorised			
4)	Steady Beacons To Be Used At Night			
5)	Cone Spacing 9m			

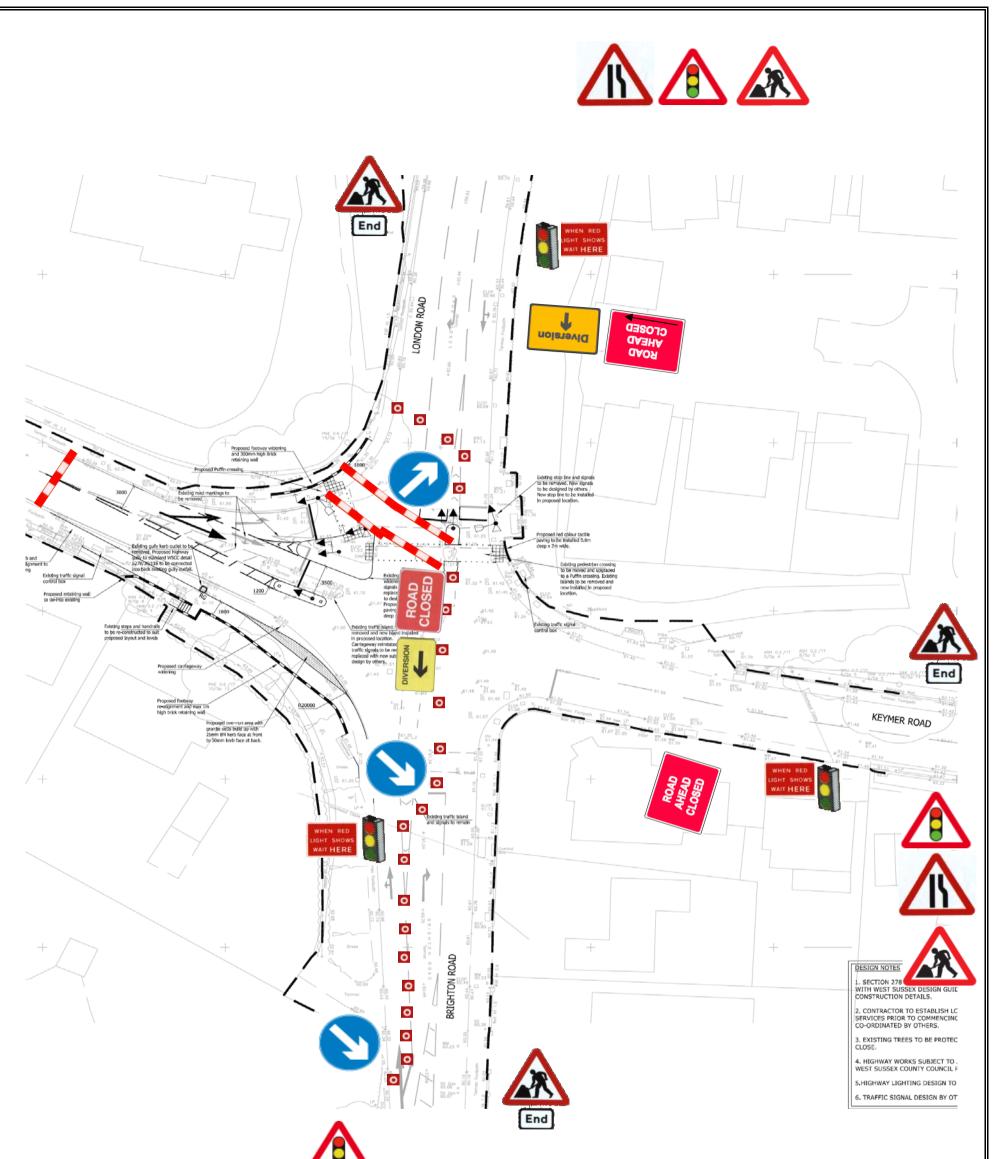

Title	Traffic Management Plans	Number	HC 16	
Project	London Road, Hassocks, New Site Entrance			
Works	S278			
1)	Cone Size : 750 mm	6)	24 Hour Traffic Lights	
	Sign Size : 750 mm			
2) 3) 4) 5)	Signs To Be Reflectorised			
4)	Steady Beacons To Be Used At Night			
-	Cone Spacing 9m			

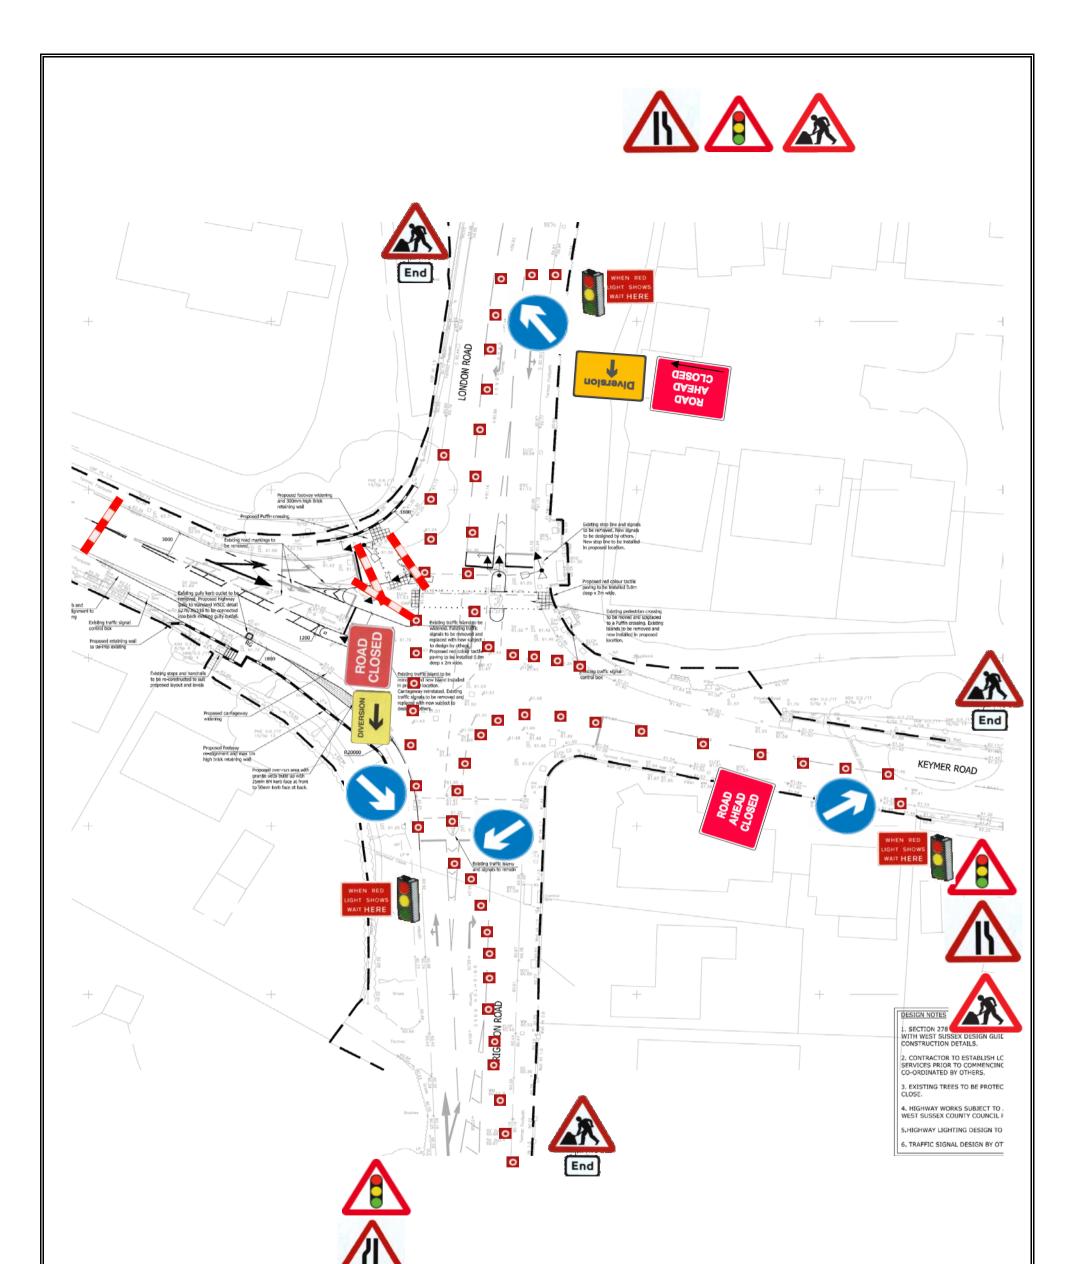

Title	Traffic Management Plans	Number	HC 17	
Project	London Road, Hassocks, New Site Entrance			
Works	S278			
1)	Cone Size : 750 mm	6)	24 Hour Traffic Lights	
2)	Sign Size :750 mm			
3)	Signs To Be Reflectorised			
4)	Steady Beacons To Be Used At Night			
5)	Cone Spacing 9m			
