Hounsome Fields, Basingstoke.

Pre Construction 24th July 2020

Hope & Clay (Construction) Ltd

Hope & Clay Construction Limited
CIVIL ENGINEERING CONTRACTORS

ID	Name	Start	Duration	Finish
1	Roundabout			
2				
3	Doormice Licence	14/09/20	20d	09/10/20
4	Tree Removal/Site Clearance	14/09/20	20d	09/10/20
5				
6	Off Line Works			
7				
8	Excavate To R/L	29/09/20	20d	26/10/20
9	Shape Embankment	29/09/20	20d	26/10/20
10	Filling to Road Profile	06/10/20	19d	30/10/20
11	Capping	13/10/20	15d	02/11/20
12	Construct Soakage Tank	22/10/20	10d	04/11/20
13	Storm Drainage	29/10/20	20d	25/11/20
14	Filter/Collection Drainage	29/10/20	20d	25/11/20
15	Kerbing	16/11/20	20d	11/12/20
16	Service Diversion???	27/10/20	40d	21/12/20
17	Gullies	23/11/20	20d	18/12/20
18	Street Lighting Ducting	14/12/20	10d	06/01/21
19	Construct Paths	14/12/20	20d	20/01/21
20	Sub Base	07/01/21	5d	13/01/21
21	Tarmac Basecourses - Hardstone	14/01/21	8d	25/01/21
22				
23	Centre Works			
24	Take Out Exisitng Northbound Carriageway	26/01/21	5d	01/02/21
25	Soakage Draiange	02/02/21	9d	12/02/21
26	Exc to R/l	02/02/21	17d	24/02/21
27	Capping	04/02/21	15d	24/02/21
28	Draiange	08/02/21	14d	25/02/21
29	Kerbing	22/02/21	10d	05/03/21
30	Gullies	24/02/21	20d	23/03/21
31	Ducting	24/02/21	20d	23/03/21
32	Sub Base	22/03/21	3d	24/03/21
33	Tarmac Basecourses - Hardstone	25/03/21	4d	30/03/21
34				
35	East Side Works			
36	Break Up old Road	31/03/21	4d	07/04/21
37	Exc to R/l	08/04/21	5d	14/04/21
38	Capping	09/04/21	6d	16/04/21
39	Drainage	14/04/21	15d	05/05/21
40	Kerbing Gullies	21/04/21	20d	19/05/21
41	Ducting	13/05/21	10d	26/05/21
42	Shape Sub Base	27/05/21	5d	03/06/21
43	Basecourses	04/06/21	4d	09/06/21
44				
45	Signage	21/04/21	30d	03/06/21
46	Street Lighting	21/04/21	30d	03/06/21
47				
48	Either Road Closure or Convoy Working	11/06/21	10d	24/06/21
49	Planning	11/06/21	4d	16/06/21
50	Wearing Courses	17/06/21	4d	22/06/21
51	Road Markings	23/06/21	2d	24/06/21
52				

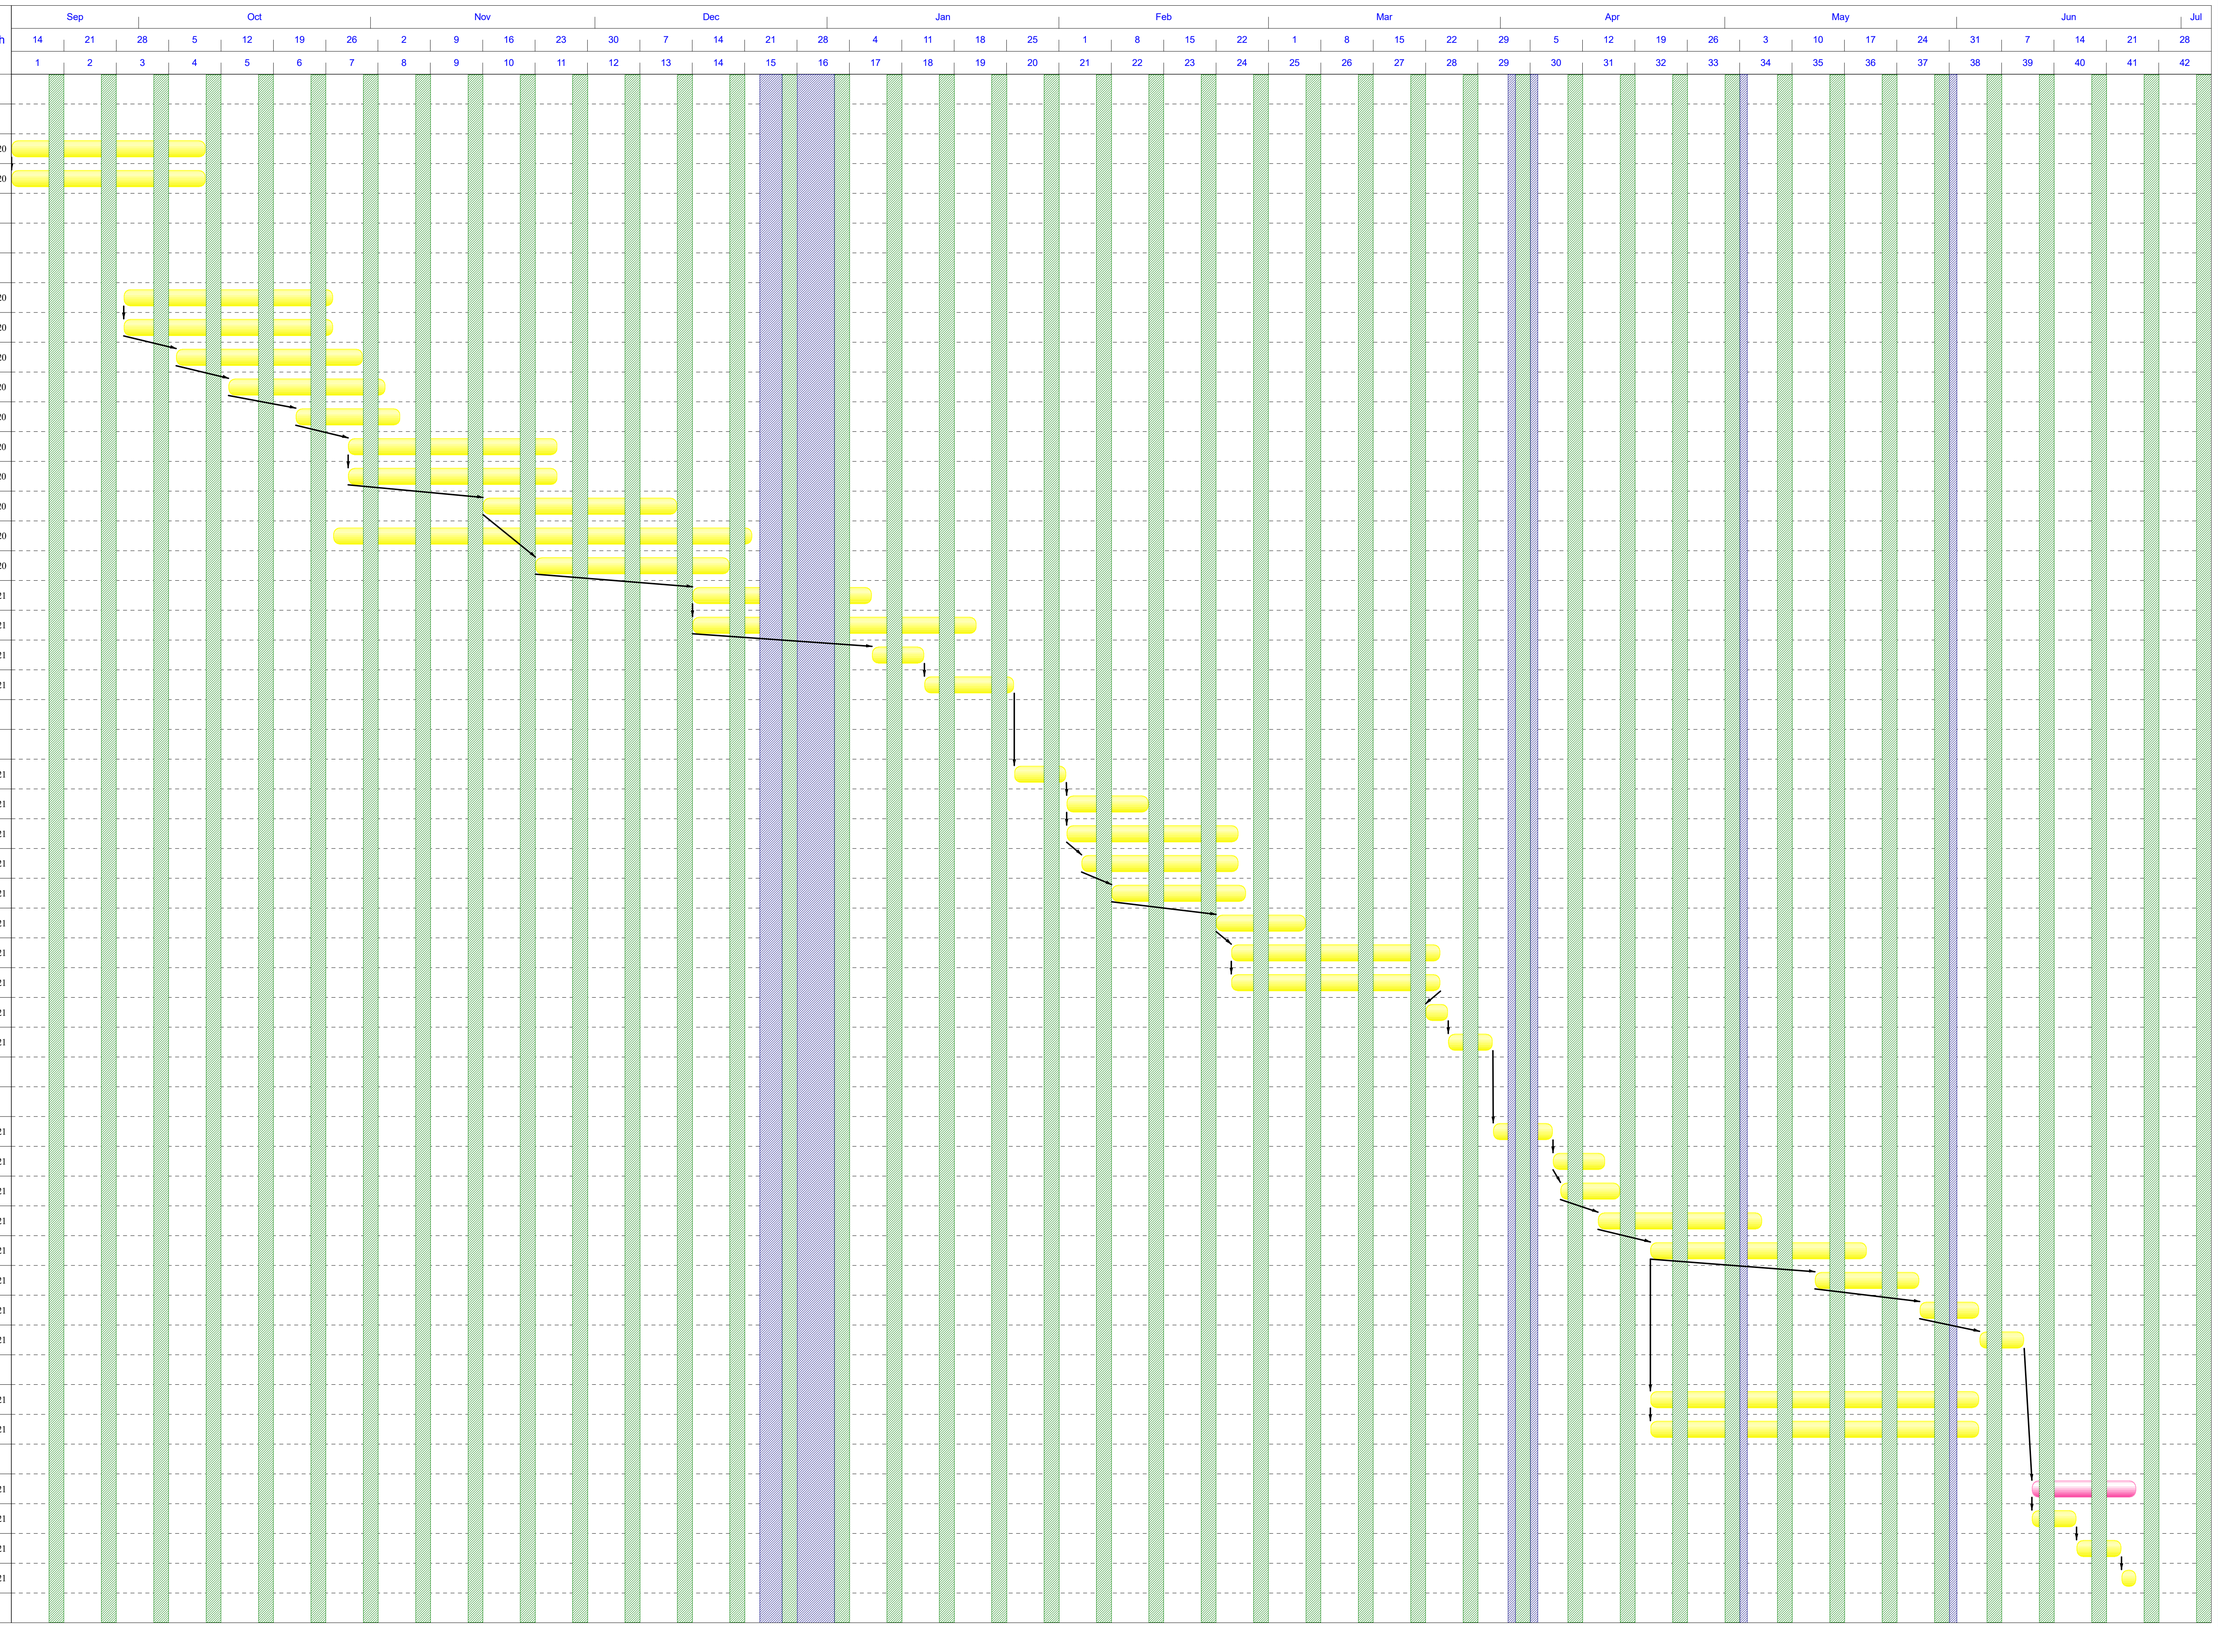

Civils Works
