Construction Rev J 12th July 2018
Option DWH First, Barratt Second, Croudace Third.
Taking Into Account New Drainage.

S278 Hook

Hope & Clay (Construction) Ltd

12/07/18

ID	Name	Start	Finish	Time
1	SGN Complete on London Road	03/09/18	03/09/18	0d
2				
3	Christmas Embargo	03/12/18	04/01/19	17d
4				
5	Set Up Site	02/08/18	03/08/18	2d
6				
7	Griffen Way			
8	Drainage HSG01-HSG03	06/08/18	31/08/18	19d
9	Drainage HSG03-Existing	03/09/18	13/09/18	9d
10	Excavate Widening	03/09/18	12/09/18	8d
11	Stone Up	03/09/18	12/09/18	8d
12	Gullies	13/09/18	18/09/18	4d
13	Street Lighting Relocations & New Columns	19/09/18	01/10/18	9d
14	Kerbing	19/09/18	05/10/18	13d
15	Breakout Kerb	08/10/18	08/10/18	1d
16	Paths & Tactiles	09/10/18	19/10/18	9d
17	Construct Island	26/10/18	30/10/18	3d
18	Signs	31/10/18	31/10/18	1d
19	Remote Path	22/10/18	25/10/18	4d
20	Basecourses	01/11/18	05/11/18	3d
21	Plane Off Wearing Course	06/11/18	07/11/18	2d
22	Lay Wearing Course	08/11/18	09/11/18	2d
23	Road Markings	12/11/18	12/11/18	1d
24				
25	Traffic Management Plan No			
26	Phase 1	06/08/18	31/08/18	19d
27	Phase 2	03/09/18	12/11/18	44d
28	Phase 3	26/10/18	26/10/18	1d
29	Phase 4	29/10/18	30/10/18	2d
30	Phase 5	22/10/18	25/10/18	4d
31				
32	Reading Road			
33	Drainage	15/10/18	09/11/18	20d
34	Excavate Widening	13/11/18	21/11/18	7d
35	Stone Up	14/11/18	26/11/18	9d
36	Gullies	27/11/18	30/11/18	4d
37	Kerbing	07/01/19	14/01/19	6d
38	Breakout Kerb	15/01/19	15/01/19	1d
39	Paths & Tactiles	16/01/19	18/01/19	3d
40	Construct Island	21/01/19	25/01/19	5d
41	Signs	28/01/19	28/01/19	1d
42	Basecourses	29/01/19	31/01/19	3d
43	Plane Off Wearing Course	01/02/19	04/02/19	2d
44	Lay Wearing Course	05/02/19	06/02/19	2d
45	Road Markings	07/02/19	08/02/19	2d
46	Street Lighting	06/02/19	15/02/19	8d
47				
48	Traffic Management Plan No			
49	Phase 1	15/10/18	09/11/18	20d
50	Phase 2	13/11/18	15/02/19	39d
51	Phase 3	21/01/19	25/01/19	5d
52	Phase 4	21/01/19	25/01/19	5d
53				
54				
55	London Road			
56	Culvert & Ditch Works	15/02/19	04/03/19	12d
57	Excavate Widening	05/03/19	08/03/19	4d
58	Stone Up	08/03/19	13/03/19	4d
59	Gullies	13/03/19	15/03/19	3d
60	Kerbing	18/03/19	25/03/19	6d
61	Breakout Kerb	22/03/19	26/03/19	3d
62	Paths & Tactiles	27/03/19	01/04/19	4d
63	Cafe Path	02/04/19	04/04/19	3d
64	Signs	05/04/19	05/04/19	1d
65	Basecourses	08/04/19	09/04/19	2d
66	Plane Off Wearing Course	10/04/19	10/04/19	1d
67	Lay Wearing Course	11/04/19	11/04/19	1d
68	Construct Island	12/04/19	16/04/19	3d
69	Road Markings	17/04/19	17/04/19	1d
70	Street Lighting	16/04/19	25/04/19	8d
71				
72	Traffic Management Plan No			
73	Phase 1 & Phase 5	15/02/19	25/04/19	39d
74	Phase 2	02/04/19	04/04/19	3d
75	Phase 3	12/04/19	16/04/19	3d
76	Phase 4	05/04/19	11/04/19	5d
77				
78				
79	A30 Street Lighting	16/04/19	24/04/19	7d
80				

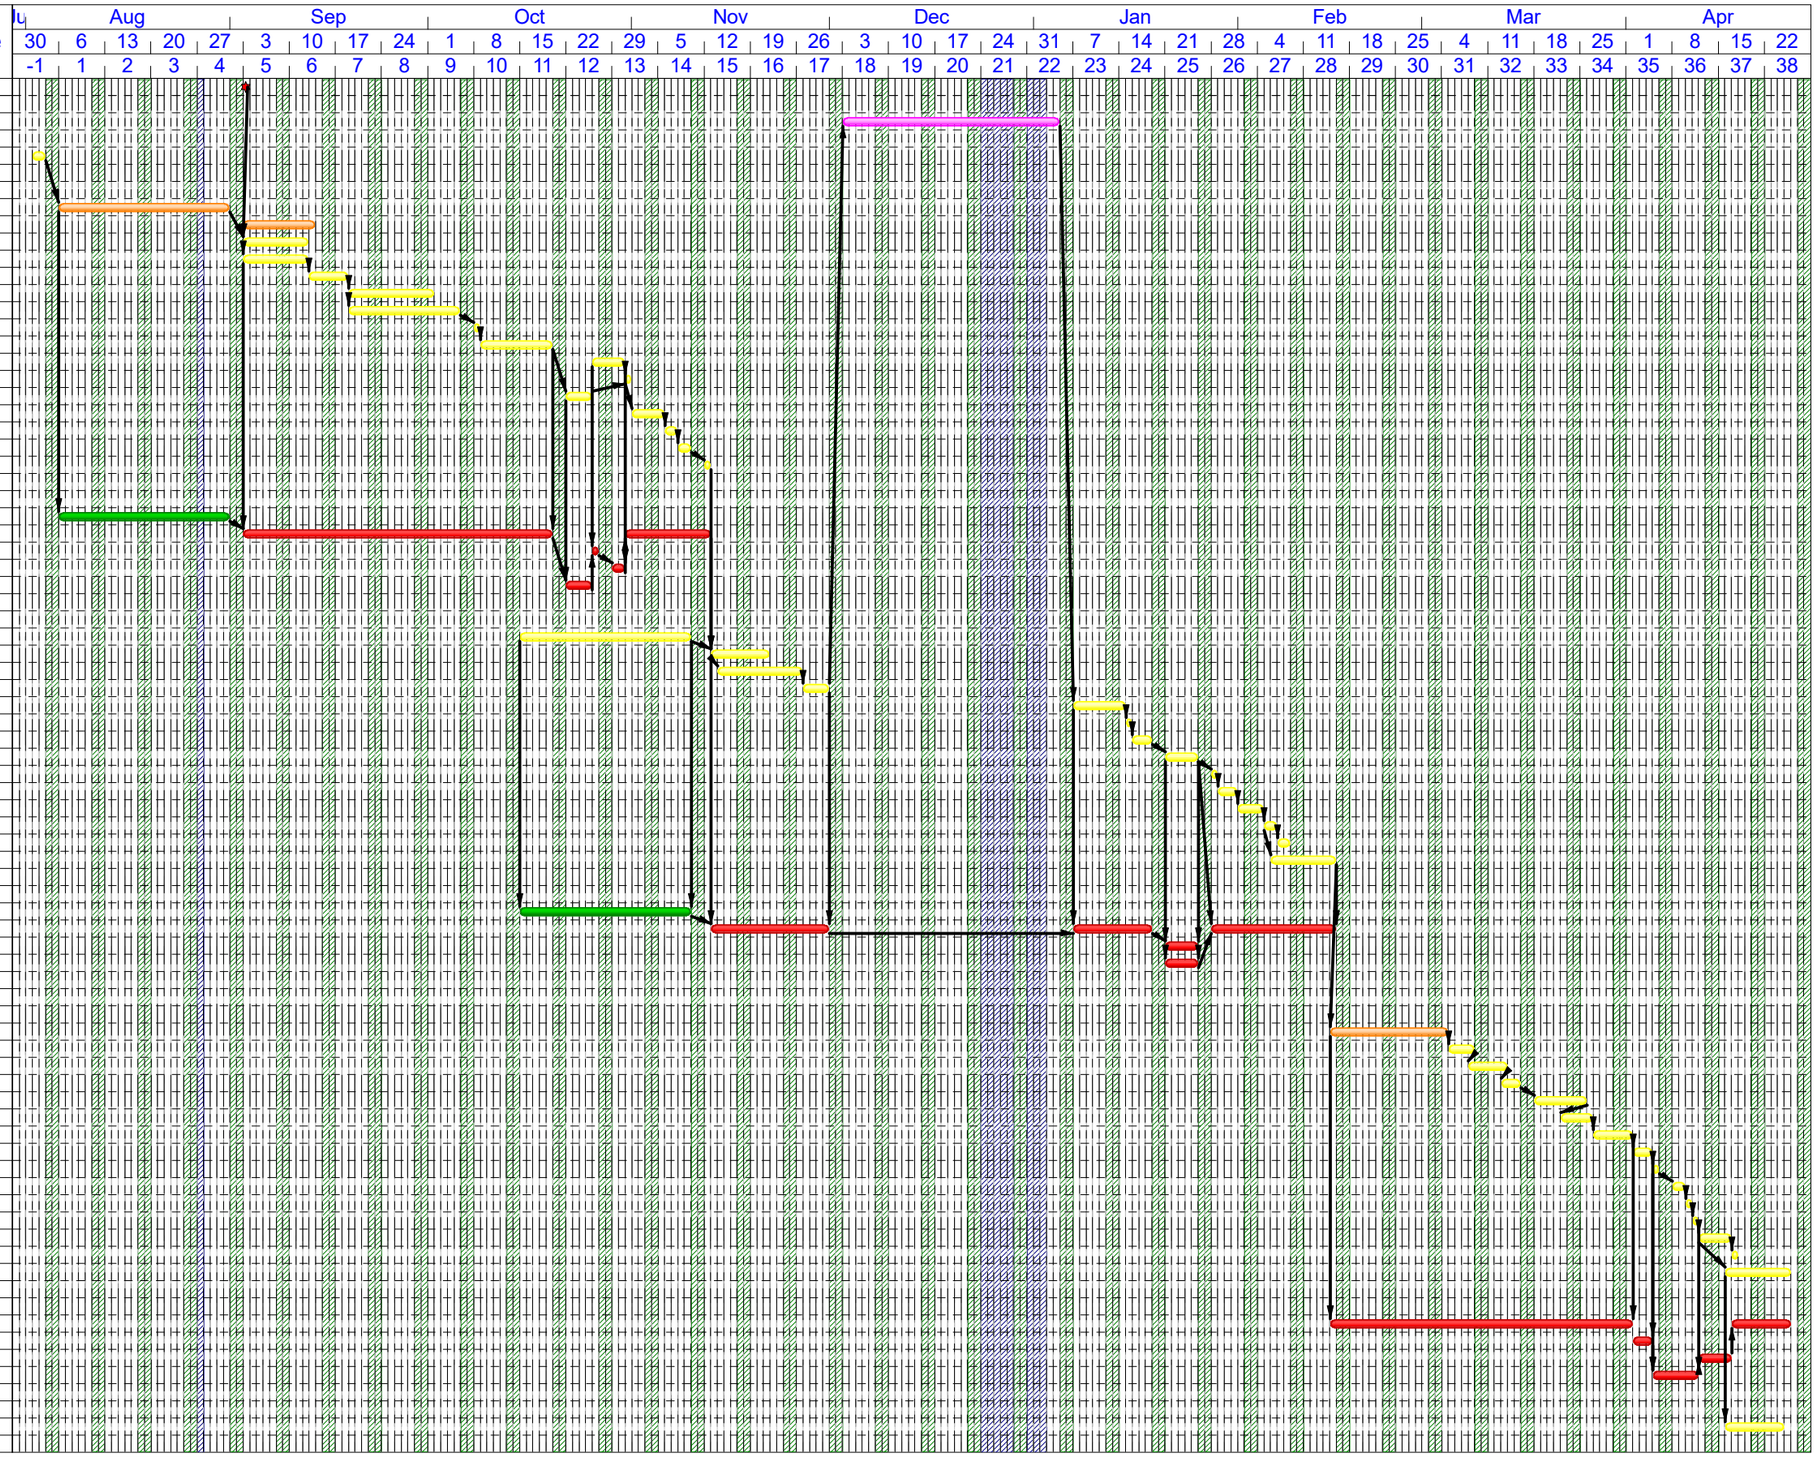

SGN Complete
Civils Work
Civils Works VO
Christmas Embargo
Non Positive Traffic Management
Positive Traffic Lights
