A30, Sainsburys Hook

Construction Issue Rev A

Hope & Clay (Construction) Ltd

ID	Name	Start	Finish	Time
1	Lead In			
2	Road Space Booking	25/07/22	02/09/22	29d
3	TTRO Application Griffin Way North & South	25/07/22	16/09/22	39d
4	TTRO Application Full Closure	25/07/22	03/03/23	151d
5	Christmas Embargo - 2 way Temp Traffic Lights	09/12/22	06/01/23	13d
6				
7	Roadspace Bookings Others			
8	HCC Griffin Way South used as Diversion route for Drainage Cleansing	25/07/22	04/08/22	9d
9	Openreach on A30	26/07/22	27/07/22	2d
10	Openreach Griffin Way South Road Closure	12/09/22	16/09/22	5d
11	A30 West of Junction Road Closure for Resurfacing	12/09/22	14/09/22	3d
12	A30 used as diversion for M3 Milnley Link Repainting	01/09/22	30/09/22	22d
13				
14	Traffic Management Phase			
15	Phase 1 HC01	03/10/22	28/10/22	20d
16	Phase 2 HC02	31/10/22	18/01/23	50d
17	Phase 3 HC03	19/01/23	31/03/23	52d
18	Phase 4 HC04	03/04/23	11/04/23	5d
19				
20	Contract Commencement	03/10/22	03/10/22	0d
21	Contract Duration	03/10/22	03/05/23	142d
22	Contract Completion	03/05/23	03/05/23	0d
23				
24	Phase 1			
25	Griffin Way North			
26	Install TM & Barriers	03/10/22	04/10/22	2d
27	Excavate to R/L	05/10/22	11/10/22	5d
28	Capping	05/10/22	11/10/22	5d
29	Storm Drainage			
30	EX-MH07	12/10/22	14/10/22	3d
31	MH07-MH06	17/10/22	19/10/22	3d
32	MH06-MH05	20/10/22	24/10/22	3d
33	MH05-MH04	25/10/22	28/10/22	4d
34	Sub Base	12/10/22	14/10/22	3d
35	Kerbing	17/10/22	01/11/22	7d
36	Gullies	24/10/22	03/11/22	9d
37	Construct Path	31/10/22	11/11/22	10d
38	Construct Island to Bellmouth	14/11/22	17/11/22	4d
39	Base & Binder to Widening	18/11/22	21/11/22	2d
40	Kerb Replacement to West Side	22/11/22	28/11/22	5d
41	Construct Path	29/11/22	19/12/22	15d
42				
43	Phase 2			
44	A30 & Griffin Way South			
45	Install Temp Traffic Lights	22/11/22	22/11/22	1d
46	South East Corner			
47	Excavate for Widening to R/L	22/11/22	28/11/22	5d
48	Capping	22/11/22	28/11/22	5d
49	Sub Base	29/11/22	30/11/22	2d
50	Kerbing	01/12/22	05/12/22	3d
51	MH09	06/12/22	07/12/22	2d
52	Gullies	08/12/22	15/12/22	6d
53				
54	Phase 2			
55	South West Corner			
56	Excavate for Widening to R/L	20/12/22	21/12/22	2d
57	Capping	20/12/22	21/12/22	2d
58	Sub Base	22/12/22	04/01/23	2d
59	Kerbing	05/01/23	09/01/23	3d
60	Gullies	10/01/23	13/01/23	4d
61				
62	Storm Drainage			
63	Ex to MH03	16/01/23	18/01/23	3d
64	MH03-MH01	19/01/23	20/01/23	2d
65	MH03-MH02	23/01/23	25/01/23	3d
66		26/01/23	30/01/23	3d
67	South Side of New Roundabout Island			
68	Saw Cut For Kerb Line	16/12/22	16/12/22	1d
69	Breakout Kerbline	19/12/22	21/12/22	3d
70	Prep for Kerbs	22/12/22	04/01/23	2d
71	Kerbing	05/01/23	06/01/23	2d
72	Gullies	22/12/22	16/01/23	10d
73				
74	Construct Southern Island	09/01/23	11/01/23	3d
75	Tactiles and Footpath Links	12/01/23	17/01/23	4d
76				
77	Swap Traffic	18/01/23	18/01/23	1d
78				
79	Phase 3			
80	North East Corner			
81	Excavate for Widening to R/L	19/01/23	20/01/23	2d
82	Capping	19/01/23	20/01/23	2d
83	Sub Base	23/01/23	24/01/23	2d
84	Kerbing	25/01/23	27/01/23	3d
85	Gullies	30/01/23	06/02/23	6d
86				
87	North West Corner			
88	Breakout Kerbs	07/02/23	08/02/23	2d
89	Prep For Kerbing	09/02/23	10/02/23	2d
90	Kerbing	13/02/23	15/02/23	3d
91				
92	Full Depth Road Construction Areas on Roundabout & London Road			
93	Plane Out	15/02/23	15/02/23	1d
94	Excavate to R/L	16/02/23	17/02/23	2d
95	Capping	20/02/23	21/02/23	2d
96	Sub Base	22/02/23	23/02/23	2d
97	Base & Binder	24/02/23	27/02/23	2d
98				
99	A30 North East Path			
100	Breakout Kerbs	28/02/23	02/03/23	3d
101	Path Construction	03/03/23	09/03/23	5d
102	Prep Kerbs	10/03/23	13/03/23	2d
103	Kerbing	14/03/23	16/03/23	3d
104				
105	Construct Islands On Roundabout.	17/03/23	31/03/23	11d
106	Street Lighting	28/02/23	31/03/23	24d
107	Signage	29/03/23	11/04/23	8d
108				
109	Plane off & Surfacing	03/04/23	11/04/23	5d
110	Road Marking	06/04/23	11/04/23	2d
111				
112	Contractors Time Risk Allowance	12/04/23	03/05/23	15d

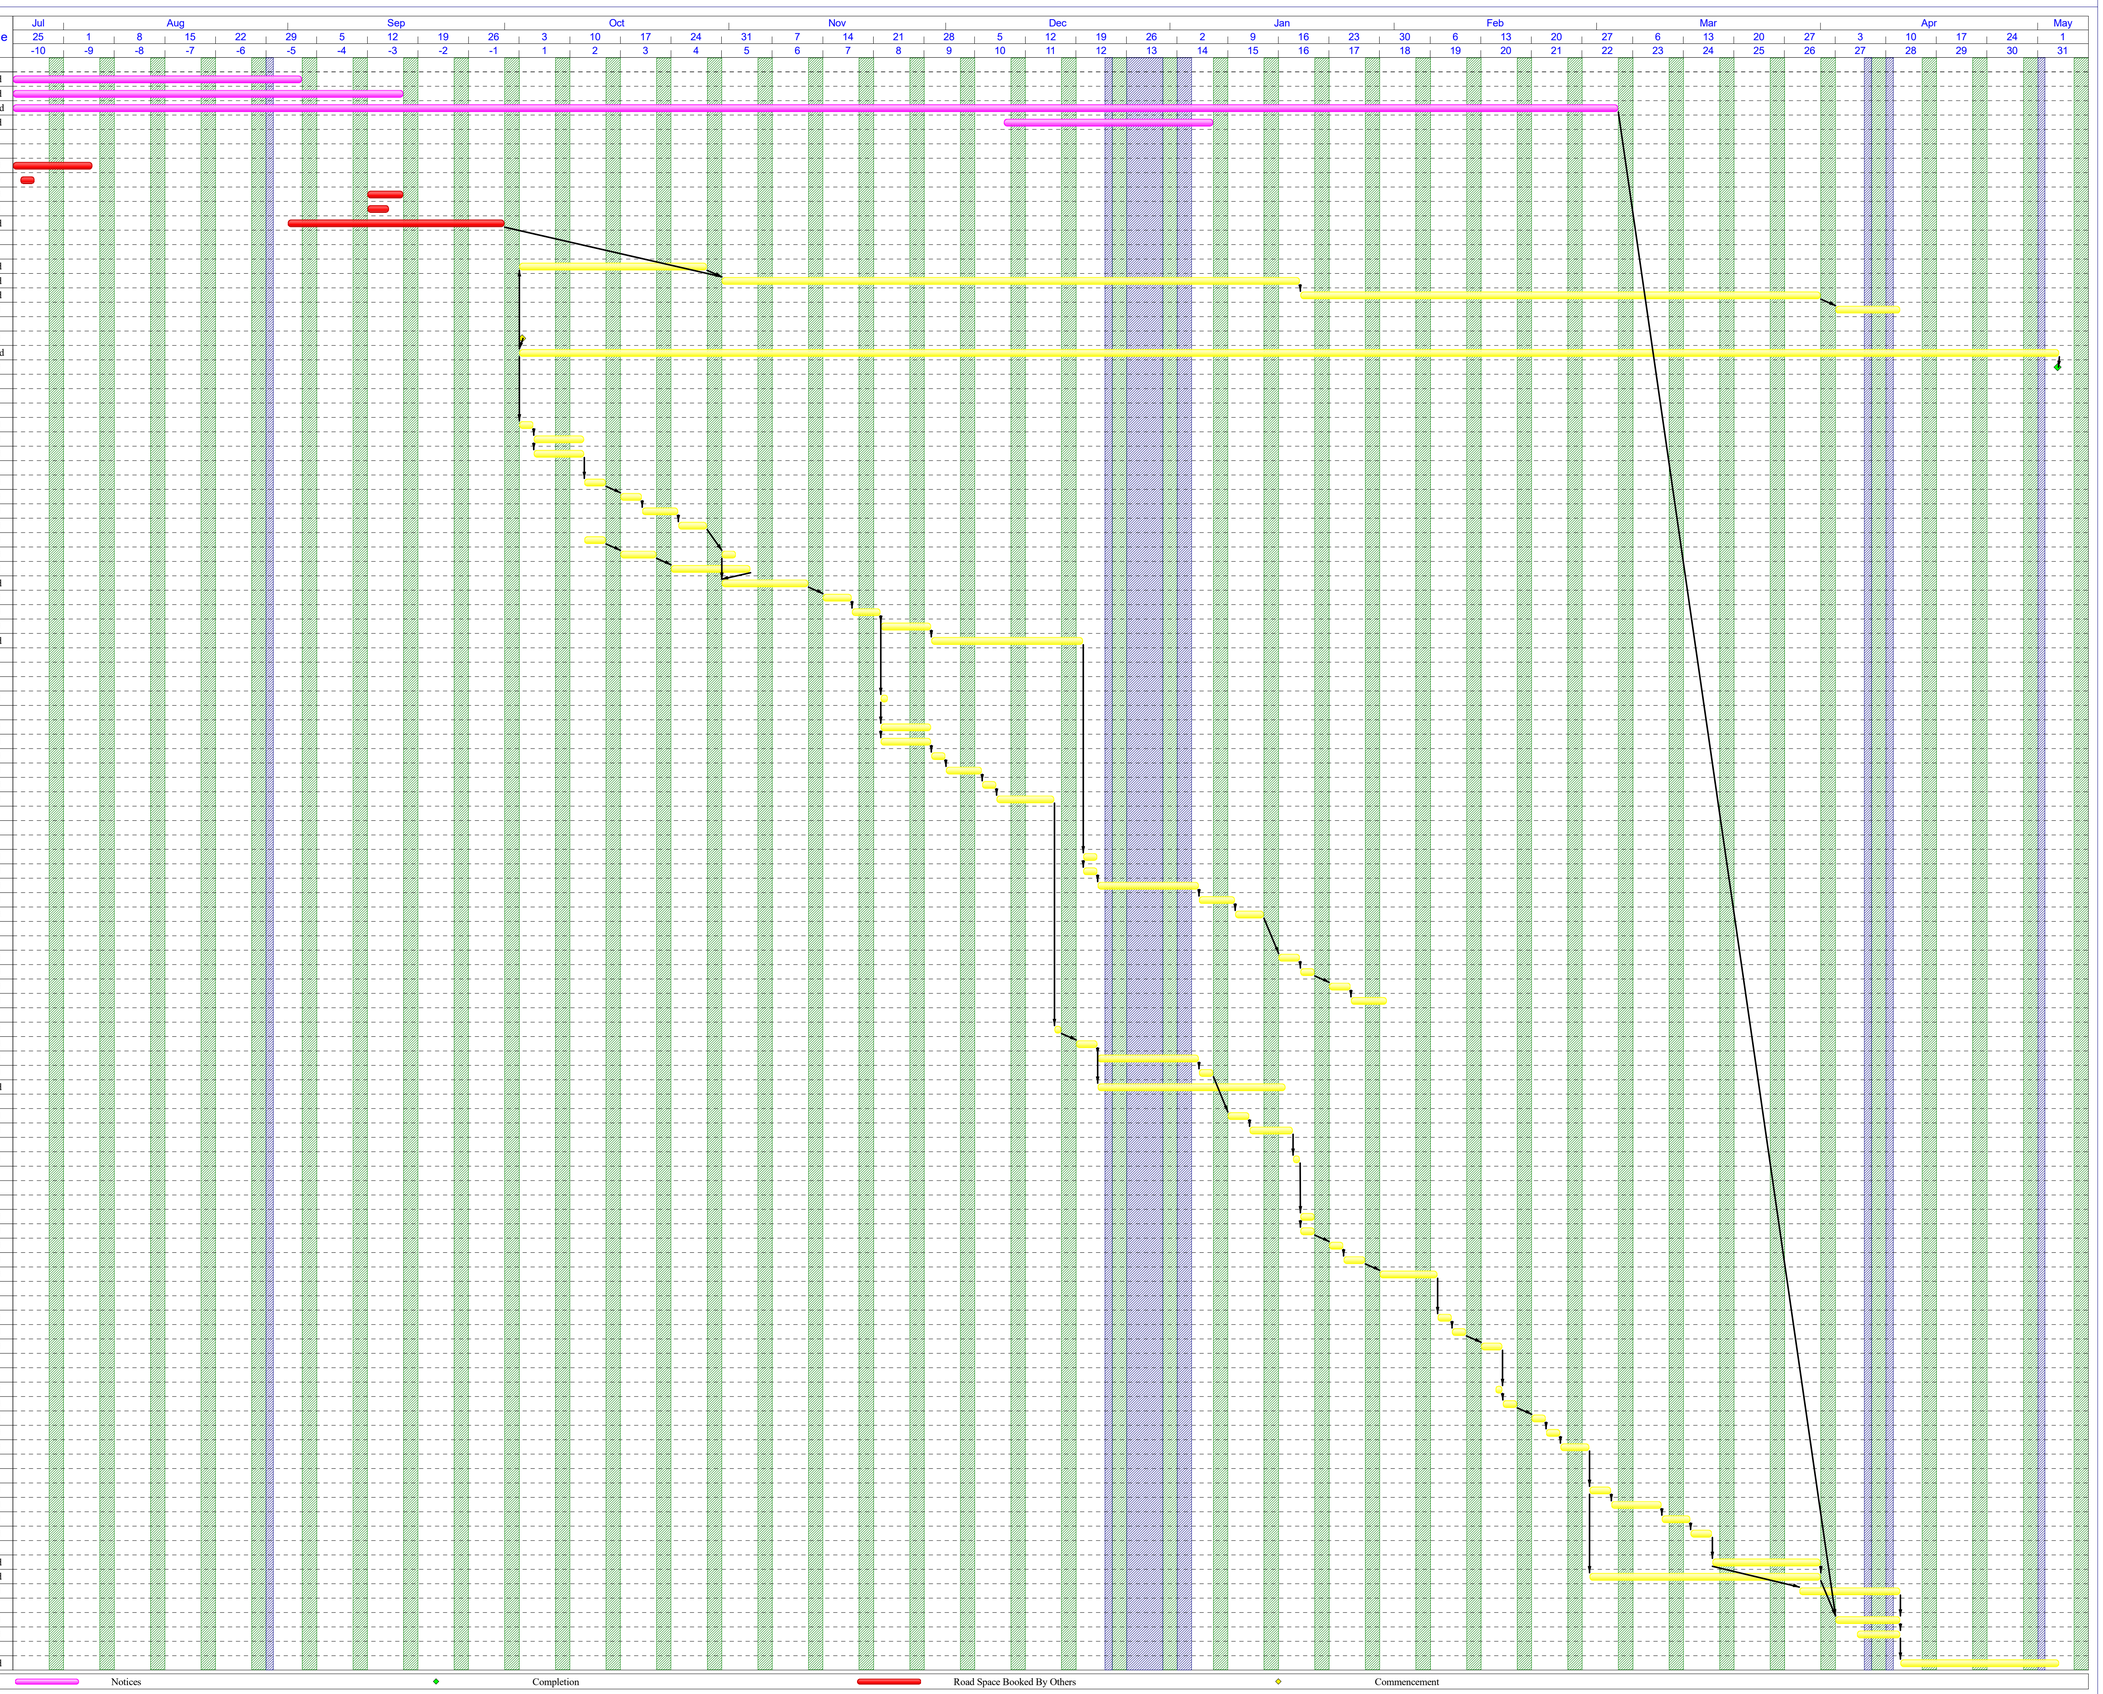

Civils | Notices | Completion | Road Space Booked By Others | Commencement
