Pre Construction Rev C

Rusty Cutter, Bedhampton Lane. S278.

Hope & Clay (Construction) Ltd

24/04/24

ID	Name	Start	Duration	Finish
1	Pre Works Planning			
2	Natural England DAS Submission	13/02/24	1d	13/02/24
3	Natural England DAS Response	11/03/24	18d	05/04/24
4	TetraTech to submit compensation area/orhid translocation proposal	05/04/24	22d	07/05/24
5	NE To Issue consent for Translocation	07/05/24	1d	07/05/24
6	Botanical Survey	11/03/24	1d	11/03/24
7	Compensation area calculation and agree with HCC	04/03/24	15d	22/03/24
8	Dormice Survey	11/03/24	1d	11/03/24
9	Agreement with HCC on the grassland compensation area in the roundabout	11/03/24	91d	19/07/24
10	S278 MWA Agreement with HVV	07/05/24	73d	16/08/24
11	Translocation of Orchids and Soils	27/08/24	4d	30/08/24
12	S278 Cycleway construction form development S278 Culvert by Gracelands	02/04/24	43d	03/06/24
13				
14	Works	20/05/24	128d	15/11/24
15	Set Up Compound	13/05/24	5d	17/05/24
16	Install Block Fencing	13/05/24	5d	17/05/24
17				
18	Bedhampton Lane			
19	Excavate to R/L	20/05/24	15d	10/06/24
20	Stone Up	20/05/24	15d	10/06/24
21	Edgings	11/06/24	8d	20/06/24
22	Install Fencing & Tactiles	21/06/24	10d	04/07/24
23				
24	Works to Ped Crossing			
25	Install Drop Crossing	21/06/24	4d	26/06/24
26	Install Island	05/07/24	3d	09/07/24
27				
28	Night Time Road Closure	12/07/24	10d	25/07/24
29	Street Lighting and Connections	12/07/24	5d	18/07/24
30	Surfacing to Path	19/07/24	5d	25/07/24
31				
32	Roundabout Works			
33	Lane Closures			
34	Works to Pedestrian Crossing Area South Bound Off Slip	19/08/24	6d	27/08/24
35	Disconnect and Relocate Column 7	26/07/24	2d	29/07/24
36	Disconnect & Install New Signage and Transfer Supply	28/08/24	3d	30/08/24
37	Excavate to R/L Footpath	02/09/24	14d	19/09/24
38	Stone Up	02/09/24	14d	19/09/24
39	Signals Nal Sockets and Ducting (Temp Signals Provided) on South Off Slip	20/09/24	10d	03/10/24
40	Signals & Duct Boxes on Roundabout Central area	20/09/24	15d	10/10/24
41	Edgings & Tactiles	11/10/24	9d	23/10/24
42				
43	Install Fencing	24/10/24	10d	06/11/24
44	Surfacing to Path	07/11/24	5d	13/11/24
45				
46	Culvert Works	26/07/24	5d	01/08/24
47	Fillling	02/08/24	9d	14/08/24
48	Construct Off Highway Path	15/08/24	9d	28/08/24
49				
50	Path on Roundabout West Bound North Bound Off Slip			
51	Excavate to R/L	24/10/24	5d	30/10/24
52	Stone Up	24/10/24	5d	30/10/24
53	Edgings	31/10/24	4d	05/11/24
54	Signals Nal Sockets and Ducting (Temp Signals Provided)	06/11/24	10d	19/11/24
55	Install Fencing & Tactiles	20/11/24	11d	04/12/24
56	Surfacing to Path			
57				
58	HA Works			
59	Plan 1 Drainage Works	29/07/24	5d	02/08/24
60	Plan 1 VRS Works	05/08/24	10d	16/08/24
61	Civils Works Plan Minor Works	19/08/24	5d	23/08/24
62	Signage	05/12/24	5d	11/12/24
63	Connections to Signage?	12/12/24	1d	12/12/24
64	Road Markings & Studs	13/12/24	4d	18/12/24
65				
66	Items to Note			
67	Footpath Closure & Diversion	20/05/24	152d	19/12/24
68	TM on Bedhampton Hill	20/05/24	49d	26/07/24
69	TM on Roundabout	29/07/24	103d	19/12/24
70	SRL Temp Traffic Lights Required SB Off Slip	29/07/24	102d	18/12/24
71	SRL Temp Traffic Lights Required SB Off Slip	22/10/24	42d	18/12/24
72	TM Required SB Off Slip	29/07/24	102d	18/12/24
73	TM Required NB Off Slip	22/10/24	43d	19/12/24

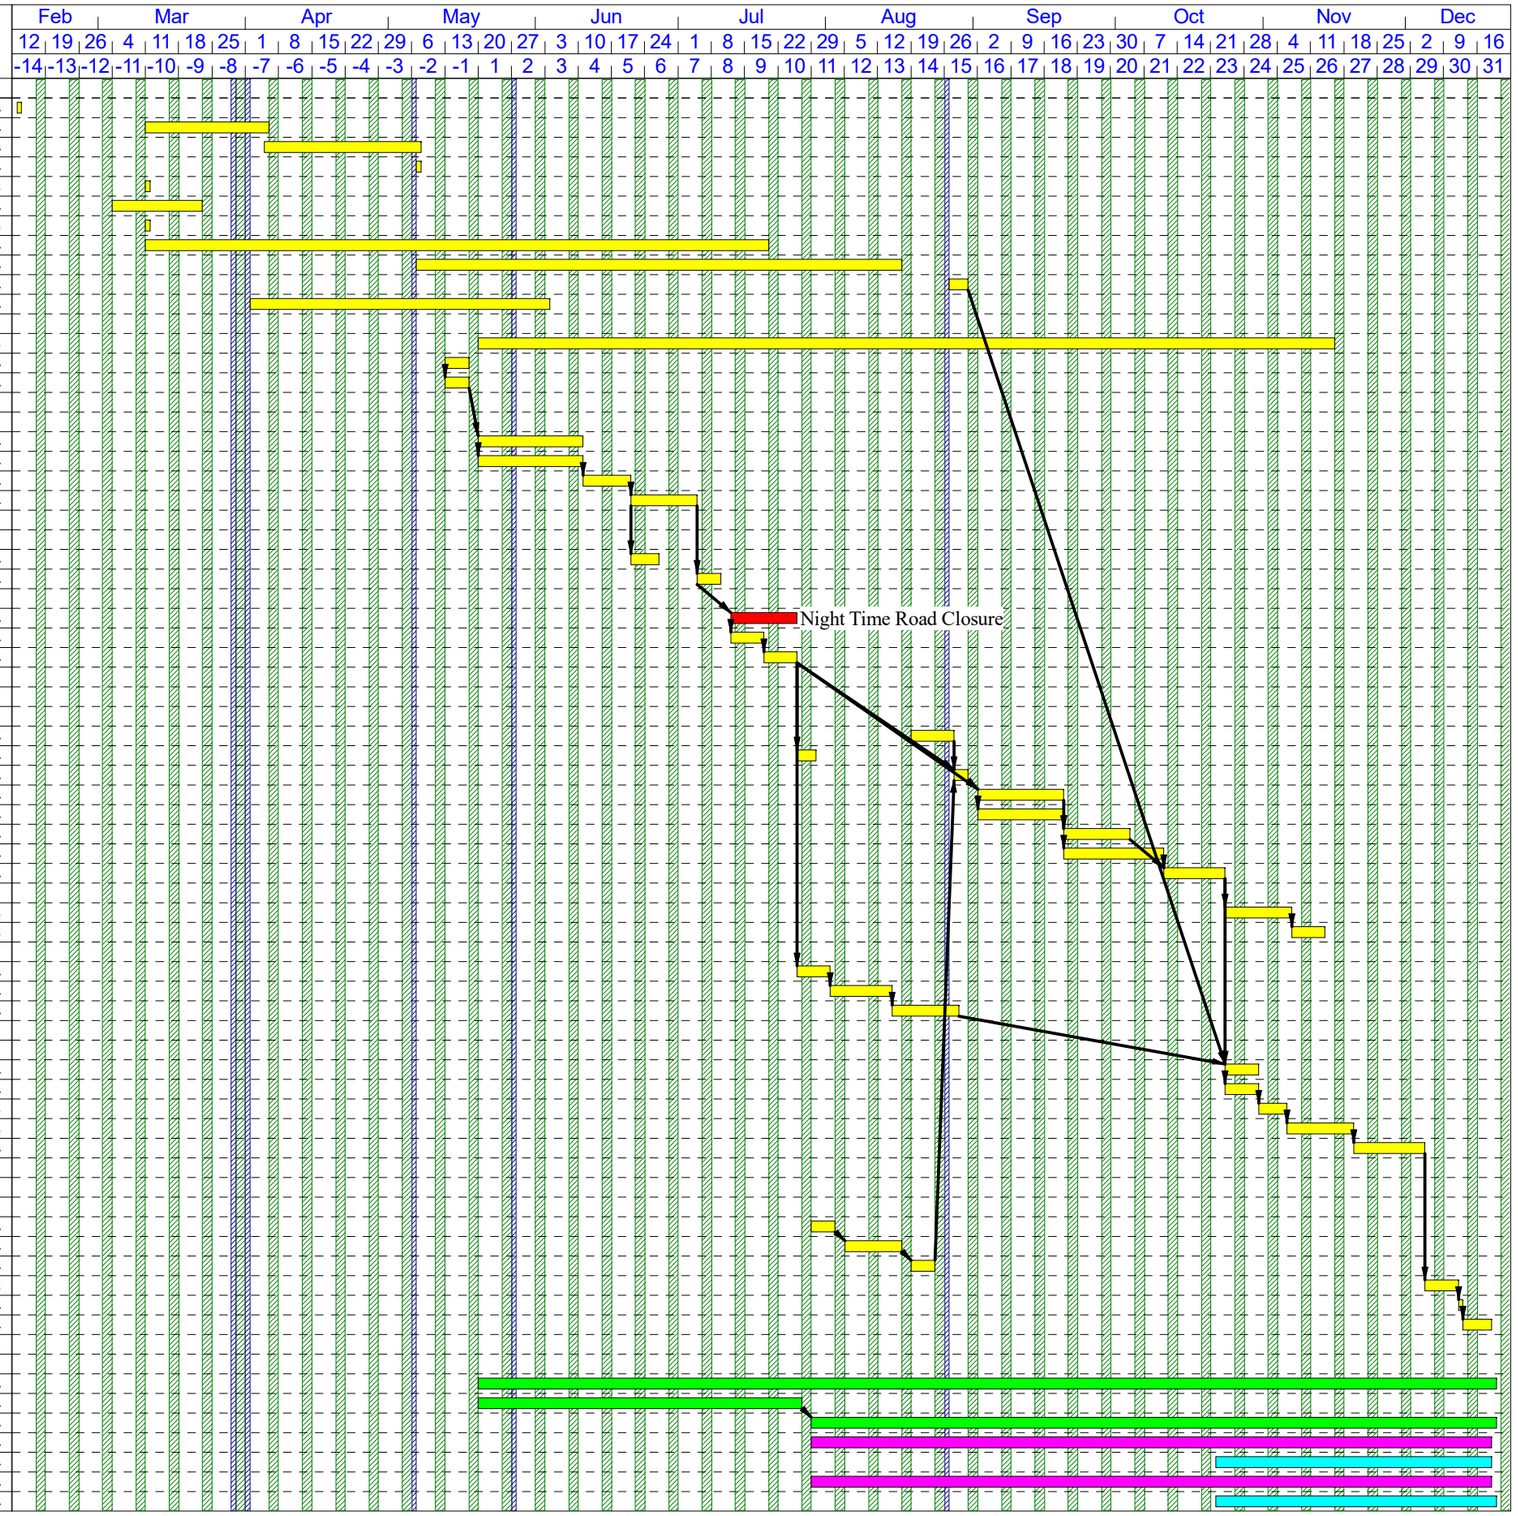

Civils | Urban 64 Temp Traffic Lights | Sector 12A/B Tm Required | Night Works | HCC TM
